




## MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: <b>04/10/2023</b>		Report No: <b>HITECH/TJN-2022-229/MT-119</b>	
Client: <b>M/S.TRUCKOMAN EQUIPMENT RENTAL LLC, OMAN</b>		Contractor: <b>N/A</b>	
Project: <b>N/A</b>		Location: <b>TER WORKSHOP-ADAM,SULTANATE OF OMAN</b>	
Procedure No. & Rev. No.: <b>HITIS/GEN/MT/01 REV.02</b>		Referencing Code / Specification: <b>ASTM E709, AWS D1.1</b>	
Acceptance Criteria: <b>AWS D1.1 ED 2021</b>		Material: <b>CS</b>	
Surface Condition: <b>As Cleaned</b>		Surface Temperature: <b>Ambient</b>	
PWHT: <b>N/A</b>			
Method: <input checked="" type="checkbox"/> Wet <input checked="" type="checkbox"/> Visible <input type="checkbox"/> Dry <input type="checkbox"/> Fluorescent		Technique: <input checked="" type="checkbox"/> Continuous <input type="checkbox"/> Residual	
Magnetization: <input checked="" type="checkbox"/> Longitudinal <input type="checkbox"/> Circular			
Equipment Type: <b>Permanent Magnetic Yoke</b>		Equipment Sr. No: <b>GAMMATEC SN00810</b>	
Cal. Validity: <b>Prior to Job</b>			
Type of Current: <b>N/A</b>		Lifting Power of Yoke: <b>18.1 KG</b>	
Sensitivity: <input checked="" type="checkbox"/> Burnah Strip <input type="checkbox"/> Pie Gauge <b>III Lines Visible</b>			
Source of Light: <b>Day light</b>		Light Intensity: <b>≥ 1000 lux min</b>	
Consumables: <b>MAGNAFLUX</b>			
Cleaner: <b>MAGNAFLUX SKC-S</b> Batch No: <b>220513 BBE</b> Validity: <b>MAY-2025</b>		White Contrast: <b>MAGNAFLUX WCP-2</b> Batch No: <b>220506 BBE</b> Validity: <b>MAY-2025</b>	
Magnetic Ink: <b>MAGNAFLUX 7HF</b> Batch No: <b>220508 BBE</b> Validity: <b>MAY-2025</b>			
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
		Sch. / WT	Observation (Map or Record of Indication)
Result (Acc./Rej.)			
<b>REGISTRATION NO &amp; OWNER ID NO:- 8615 DA / PLM 1029 (LORRY LOADER CRANE LIFTING HOOK)</b>			
<b>LORRY LOADER CRANE HOOK MPI (HOOK SL NO: FT29-10-14)</b>	<b>N/A</b>	<b>N/A</b>	<b>N/A</b>
<b>N/A</b>	<b>N/A</b>	<b>N/A</b>	<b>N/A</b>
<b>NO RELEVANT INDICATION OBSERVED</b>			<b>ACCEPTABLE</b>

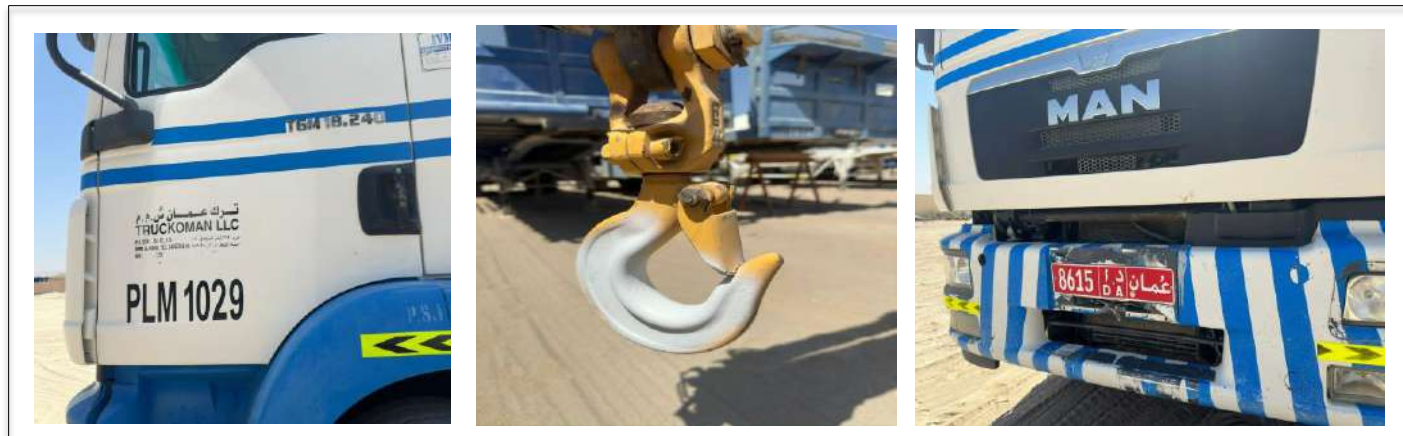

**"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"**

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:		<b>03/10/2024</b>
Hi-Tech Inspection Services LLC	Contractor	Client/ TPI /AI
Signature:  	Signature:	Signature:
Name: <b>ANUJ KUMAR</b>	Name:	Name:
Qualification: <b>MPT Level II</b>		
Date: <b>04/10/2023</b>	Date:	Date
