


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 22/09/2025		Report No: HITECH/TJN-2025-467/MT-110	
Client: M/S. TRUCKOMAN EQUIPMENT RENTAL LLC, OMAN		Contractor: N/A	
Project: N/A		Location: NIZWA, SULTANATE OF OMAN	
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.05		Referencing Code / Specification: ASTM E709, AWS D1.1	
Acceptance Criteria: AWS D1.1 ED 2020		Material: N/A	
Surface Condition: Acceptable		Surface Temperature: Ambient	
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual	
Equipment Type: Permanent Magnetic Yoke		PWHT: N/A	
Equipment Sr. No: GAMMATEC 00836		Magnetization: ☒ Longitudinal ☐ Circular	
Type of Current: N/A		Cal. Validity: Prior to Job	
Lifting Power of Yoke: 18.1 Kg		Sensitivity: ☒ Burmah Strip ☐ Pie Gauge III Lines Visible	
Source of Light: Day light		Light Intensity: ≥ 1000 lux min	
Consumables: MAGNAFLUX			
Cleaner: MAGNAFLUX SKC-S		White contrast: MAGNAFLUX WCP-2	
Batch No: 240706 BBE		Batch No: 240702 BBE	
Validity: JULY-2027		Validity: JULY-2027	
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
Sch. / WT		Observation (Map or Record of Indication)	
Result (Acc./Rej.)			
REGISTRATION NO & OWNER ID NO: - 9582 YM / TER 1098 (PRIME MOVER FIFTH WHEEL)			
FIFTH WHEEL MAKE: JOST SL NO: 202306000006	N/A	N/A	N/A
NO RELEVANT INDICATION OBSERVED		ACCEPTED	

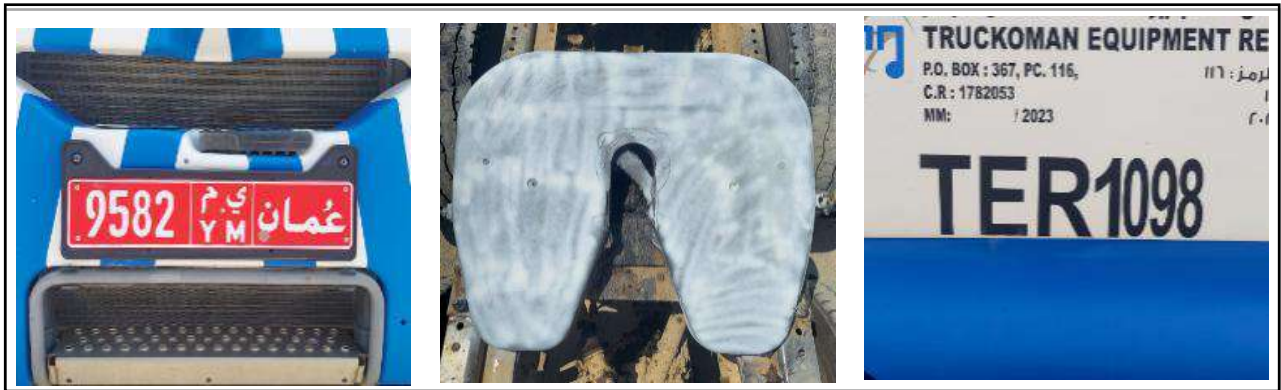

"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:

21/09/2026

Hi-Tech Inspection Services LLC		Contractor		Client	
Signature:		Signature:		Signature:	
					
Name: JENSON DASS		Name:		Name:	
Qualification: NDT Level II					
Date: 22/09/2025		Date:		Date	
