


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 23/11/2022		Report No: HITECH/TJN-2022-229/MT-041	
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL. LLC		Contractor: N/A	
Project: N/A		Location: TRUCKOMAN WORKSHOP-ADAM, SULTANATE OF OMAN	
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.02		Referencing Code / Specification: AWS D1.1 ED 2015	
Acceptance Criteria: AWS D1.1 ED 2015		Material: CS	
Surface Condition: Acceptable		Surface Temperature: Ambient	
PWHT: N/A			
Method: ☐ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual	
Magnetization: ☒ Longitudinal ☐ Circular			
Equipment Type: Permanent Magnetic Yoke		Equipment Sr. No: GAMMATEC 0860	
Cal. Validity: Prior to Job			
Type of Current: N/A		Lifting Power of Yoke: 18.1 KG	
Sensitivity: ☒ Burnah Strip ☐ Pie Gauge III Lines Visible			
Source of Light: Day light		Light Intensity: ≥ 1000 lux min	
Consumables: MAGNAFLUX			
Cleaner : MAGNAFLUX SKC-S		White contrast : MAGNAFLUX WCP-2	
Batch No: 211109		Batch No: 211107	
Validity: NOV-2024		Validity: NOV-2024	
Magnetic Ink : MAGNAFLUX 7 HF		Batch No: 211101	
Validity: NOV-2024			
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
Sch. / WT		Observation (Map or Record of Indication)	
Result (Acc./Rej.)			
REGISTRATION NO & OWNER ID NO: - 749MR / PLM1958			
KING PIN & FILLET WELD MAKE: JOST 3.5" TYPE: KZ-14	I SHAPED CYLINDRICAL KING PIN, TOP HEAD 114MMØ, INTERMEDIATE 89MMØ, BOTTOM HEAD 111MMØ		NO RELEVANT INDICATION OBSERVED
		ACCEPTED	

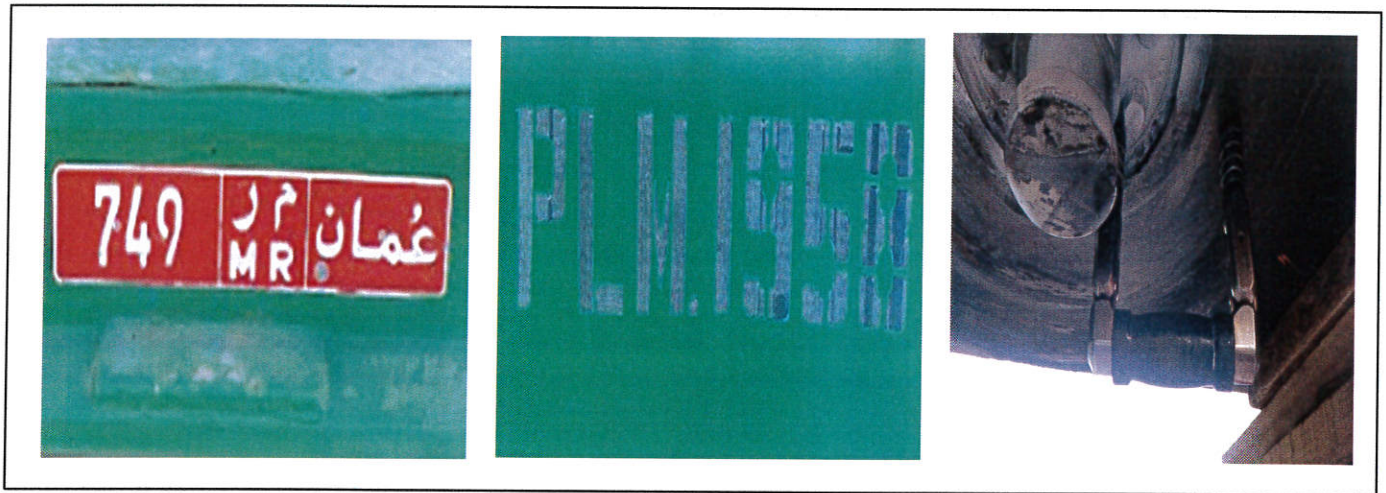

MPI CARRIED OUT ON ABOVE MENTIONED ITEMS (FEASIBLE AREA ONLY)

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:

22/11/2023

Hi-Tech Inspection Services LLC

Contractor

Client/ TPI /AI

Signature:

Signature:

Signature:

Name: **LAKSHMANDAS.M**

Name:

Name:

Qualification: **MPT Level II**

Date: **23/11/2022**

Date:

Date
