


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 02/07/2023				Report No: HITECH/TJN-2022-229/MT-074			
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL LLC,OMAN				Contractor: N/A			
Project: N/A				Location: ADAM WORKSHOP,SULTANATE OF OMAN			
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.02				Referencing Code / Specification: ASTM E709, AWS D1.1			
Acceptance Criteria: AWS D1.1 ED 2021				Material: CS			
Surface Condition: Acceptable		Surface Temperature: Ambient		PWHT: N/A			
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual		Magnetization: ☒ Longitudinal ☐ Circular			
Equipment Type: Permanent Magnetic Yoke		Equipment Sr. No: GAMMATEC 00836		Cal. Validity: Prior to Job			
Type of Current: N/A		Lifting Power of Yoke: 18.1 KG		Sensitivity: ☒ Burnish Strip ☐ Pie Gauge III Lines Visible			
Source of Light: Day light				Light Intensity: ≥ 1000 lux min			
Consumables: MAGNAFLUX							
Cleaner : MAGNAFLUX SKC-S Batch No: 220513 Validity: MAY-2025		White contrast : MAGNAFLUX WCP-2 Batch No: 220506 Validity: MAY-2025		Magnetic Ink : MAGNAFLUX 7 HF Batch No: 220508 Validity: MAY-2025			
Item: Description/Line No./ Drawing No.	Weld No	Welder No	Size	Sch. / WT	Observation (Map or Record of Indication)		Result (Acc./Rej.)
REGISTRATION NO & OWNER ID NO: - 4725 MK / TER 254							
KING PIN & FILLET WELD MAKE: JOST TYPE:KZ-14	I SHAPED CYLINDRICAL KING PIN, TOP HEAD 114MM ϕ , INTERMEDIATE 89MM ϕ , BOTTOM HEAD 111MM ϕ			NO RELEVANT INDICATION OBSERVED		ACCEPTED	



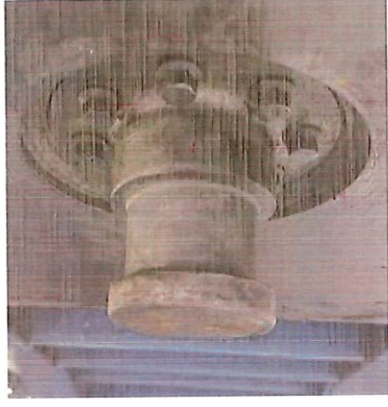

"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"		
LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:		01/07/2024
Hi-Tech Inspection Services LLC	Contractor	Client/ TPI /AI
Signature:	Signature:	Signature:
Name: LAKSHMANDAS.M	Name:	Name:
Qualification: MPT Level II	Date:	Date
Date: 02/07/2023		
