


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 04/07/2023		Report No: HITECH/TJN-2022-229/MT-080	
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL LLC,OMAN		Contractor: N/A	
Project: N/A		Location: TRUCKOMAN WORKSHOP-ADAM, SULTANATE OF OMAN	
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.02		Referencing Code / Specification: ASTM E709,AWS D1.1	
Acceptance Criteria: AWS D1.1 ED 2021		Material: CS	
Surface Condition: Acceptable		Surface Temperature: Ambient	
PWHT: N/A			
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual	
Magnetization: ☒ Longitudinal ☐ Circular			
Equipment Type: Permanent Magnetic Yoke		Equipment Sr. No: GAMMATEC 00836	
Cal. Validity: Prior to Job			
Type of Current: N/A		Lifting Power of Yoke: 18.1 KG	
Sensitivity: ☒ Burnah Strip ☐ Pie Gauge III Lines Visible			
Source of Light: Day light		Light Intensity: ≥ 1000 lux min	
Consumables: MAGNAFLUX			
Cleaner : MAGNAFLUX SKC-S		White contrast : MAGNAFLUX WCP-2	
Batch No: 220513		Batch No: 220506	
Validity: MAY-2025		Validity: MAY-2025	
Magnetic Ink : MAGNAFLUX 7 HF		Batch No: 220508	
Validity: MAY-2025			
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
		Sch. / WT	Observation (Map or Record of Indication)
			Result (Acc./Rej.)
REGISTRATION NO & OWNER ID NO:- 6908 DS / TER 1051			
FIFTH WHEEL MAKE: JOST TYPE : JSK 38C SERIAL NO: 13038617-63	N/A	N/A	N/A
			N/A
			NO RELEVANT INDICATION OBSERVED
			ACCEPTED

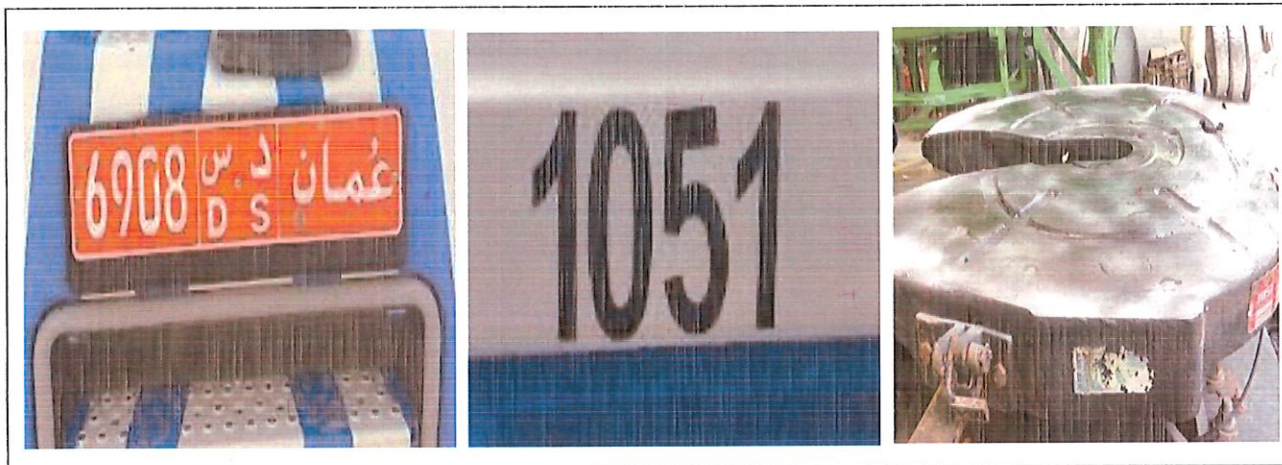

"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:

03/07/2024

Hi-Tech Inspection Services LLC

Contractor

Client/ TPI /AI

Signature:




Signature:

Signature:

Name: LAKSHMANDAS

Name:

Name:

Qualification: MPT Level II

Date:

Date

Date: 04/07/2023

HITECH-NDT-F-87-MT-01
