


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 04/07/2023				Report No: HITECH/TJN-2022-229/MT-083			
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL LLC,OMAN				Contractor: N/A			
Project: N/A				Location: TRUCKOMAN WORKSHOP-ADAM, SULTANATE OF OMAN			
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.02				Referencing Code / Specification: ASTM E709,AWS D1.1			
Acceptance Criteria: AWS D1.1 ED 2021				Material: CS			
Surface Condition: Acceptable		Surface Temperature: Ambient			PWHT: N/A		
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual			Magnetization: ☒ Longitudinal ☐ Circular		
Equipment Type: Permanent Magnetic Yoke		Equipment Sr. No: GAMMATEC 00836			Cal. Validity: Prior to Job		
Type of Current: N/A		Lifting Power of Yoke: 18.1 KG		Sensitivity: ☒ Burnah Strip ☐ Pie Gauge III Lines Visible			
Source of Light: Day light				Light Intensity: ≥ 1000 lux min			
Consumables: MAGNAFLUX							
Cleaner : MAGNAFLUX SKC-S		White contrast : MAGNAFLUX WCP-2			Magnetic Ink : MAGNAFLUX 7 HF		
Batch No: 220513		Batch No: 220506			Batch No: 220508		
Validity: MAY-2025		Validity: MAY-2025			Validity: MAY-2025		
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size	Sch. / WT	Observation (Map or Record of Indication)		Result (Acc./Rej.)
REGISTRATION NO & OWNER ID NO:- 9070 RK / TER 1053							
FIFTH WHEEL MAKE: JOST TYPE : JSK 38C SERIAL NO: 13131832-63	N/A	N/A	N/A	N/A	NO RELEVANT INDICATION OBSERVED		ACCEPTED

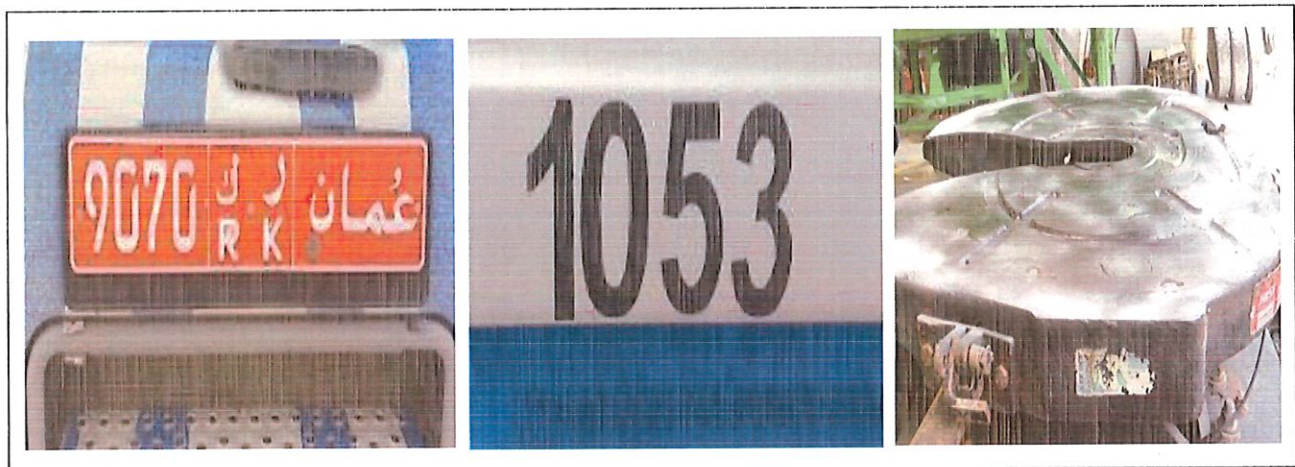

"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"		
LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:		03/07/2024
Hi-Tech Inspection Services LLC	Contractor	Client/ TPI /AI
Signature: 	Signature:	Signature:
Name: LAKSHMANDAS	Name:	Name:
Qualification: MPT Level II		
Date: 04/07/2023	Date:	Date

HITECH-NDT-F-87-MT-01
