


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 10/11/2022		Report No: HITECH/TJN-2022-229/MT-040	
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL. LLC		Contractor: N/A	
Project: N/A		Location: TRUCKOMAN WORKSHOP-ADAM, SULTANATE OF OMAN	
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.02		Referencing Code / Specification: AWS D1.1 ED 2015	
Acceptance Criteria: AWS D1.1 ED 2015		Material: CS	
Surface Condition: Acceptable		Surface Temperature: Ambient	
Method: ☐ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual	
Equipment Type: Permanent Magnetic Yoke		PWHT: N/A	
Equipment Sr. No: GAMMATEC 0860		Magnetization: ☒ Longitudinal ☐ Circular	
Type of Current: N/A		Cal. Validity: Prior to Job	
Lifting Power of Yoke: 18.1 KG		Sensitivity: ☒ Burnah Strip ☐ Pie Gauge III Lines Visible	
Source of Light: Day light		Light Intensity: ≥ 1000 lux min	
Consumables: MAGNAFLUX			
Cleaner : MAGNAFLUX SKC-S Batch No: 211109 Validity: NOV-2024		White contrast : MAGNAFLUX WCP-2 Batch No: 211107 Validity: NOV-2024	
Magnetic Ink : MAGNAFLUX 7 HF Batch No: 211101 Validity: NOV-2024			
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
		Sch. / WT	Observation (Map or Record of Indication)
			Result (Acc./Rej.)
REGISTRATION NO & OWNER ID NO: - 8866 YW / TER1638			
KING PIN & FILLET WELD MAKE: JOST 3.5" TYPE: KZ-14	I SHAPED CYLINDRICAL KING PIN, TOP HEAD 114MMØ, INTERMEDIATE 89MMØ, BOTTOM HEAD 111MMØ		NO RELEVANT INDICATION OBSERVED
			ACCEPTED

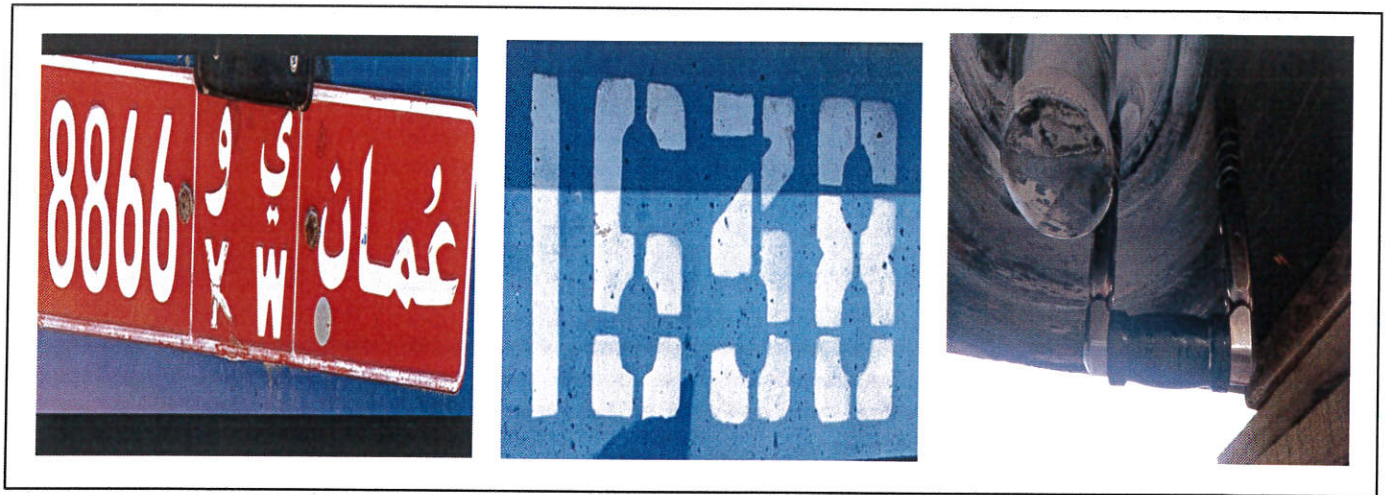

MPI CARRIED OUT ON ABOVE MENTIONED ITEMS (FEASIBLE AREA ONLY)

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:

09/11/2023

Hi-Tech Inspection Services LLC

Contractor

Client/ TPI /AI

Signature:

Signature:

Signature:

Name: **N.SREEKUMAR**

Name:

Name:

Qualification: **MPT Level II**

Date: **10/11/2022**

Date:

Date
