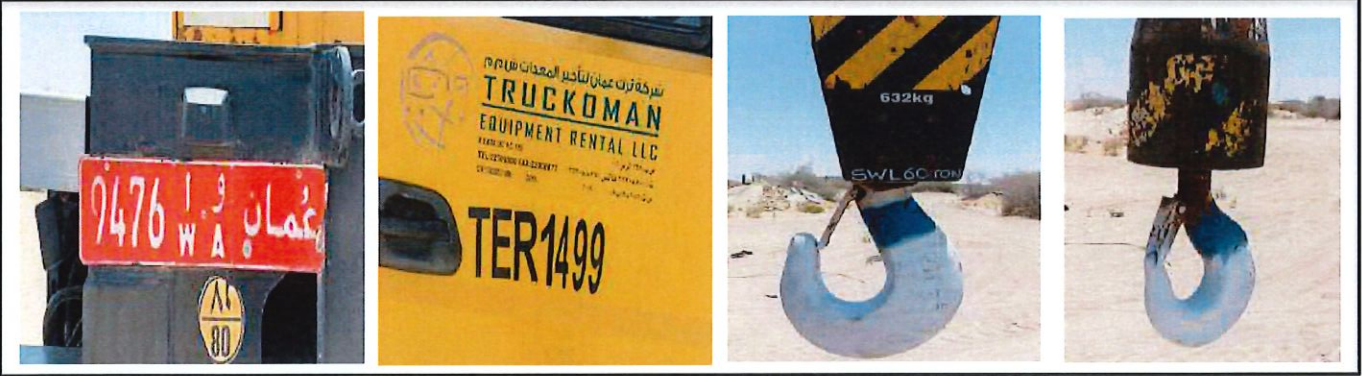


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 06/05/2025		Report No: HITECH/TJN-2025-467/MT-002	
Client: M/S.TRUCKOMAN EQUIPMENT RENTAL LLC, OMAN		Contractor: N/A	
Project: N/A		Location: TER WORKSHOP-ADAM,SULTANATE OF OMAN	
Procedure No. & Rev. No.: HITIS/GEN/MT/01 REV.05		Referencing Code / Specification: ASTM E709, AWS D1.1	
Acceptance Criteria: AWS D1.1 ED 2020		Material: CS	
Surface Condition: As Cleaned		Surface Temperature: Ambient	
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual	
PWHT: N/A		Magnetization: ☒ Longitudinal ☐ Circular	
Equipment Type: Permanent Magnetic Yoke		Equipment Sr. No: GAMMATEC SN00810	
Type of Current: N/A		Cal. Validity: Prior to Job	
Lifting Power of Yoke: 18.1 KG		Sensitivity: ☐ Burmah Strip ☒ Pie Gauge III Lines Visible	
Source of Light: Day light		Light Intensity: ≥ 1000 lux min	
Consumables: MAGNAFLUX			
Cleaner: MAGNAFLUX SKC-S Batch No: 230602 BBE Validity: JUN-2026		White Contrast: MAGNAFLUX WCP-2 Batch No: 230605 BBE Validity: MAY-2026	
Magnetic Ink: MAGNAFLUX 7HF Batch No: 230604 BBE Validity: JUN-2026			
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size
		Sch. / WT	Observation (Map or Record of Indication)
			Result (Acc./Rej.)
REGISTRATION NO & OWNER ID NO:- 9476 WA / TER 1499 (MOBILE CRANE LIFTING HOOKS)			
CRANE MAIN HOOK ID NO: HCZ1860436 HOOK CAPACITY 60.0 T	N/A	N/A	N/A
			NO RELEVANT INDICATION OBSERVED
CRANE AUX.HOOK ID NO: 12386433 HOOK CAPACITY 5.0 T	N/A	N/A	N/A
			NO RELEVANT INDICATION OBSERVED
			
"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"			
LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:		06/05/2026	
Hi-Tech Inspection Services LLC		Contractor	
Client/ TPI /AI			
Signature:	Signature:	Signature:	
			
Name: LAKSHMANDAS.M	Name:	Name:	
Qualification: MPT Level II			
Date: 06/05/2025	Date:	Date:	
