


MAGNETIC PARTICLE EXAMINATION REPORT

Date of Examination: 30/12/2025		Report No: HITECH/TJN-2025-467/MT-136				
Client: M/S. TRUCKOMAN EQUIPMENT RENTAL LLC, OMAN		Contractor: N/A				
Project: N/A		Location: MARMUL, SULTANATE OF OMAN				
Procedure No. & Rev. No.: HITECH-TPI-P-T-253-MT-14		Referencing Code / Specification: ASME E709 / AWS D1.1				
Acceptance Criteria: AWS D1.1		Material: N/A				
Surface Condition: Acceptable		Surface Temperature: Ambient				
PWHT: N/A						
Method: ☒ Wet ☒ Visible ☐ Dry ☐ Fluorescent		Technique: ☒ Continuous ☐ Residual				
Magnetization: ☒ Longitudinal ☐ Circular						
Equipment Type: Permanent Yoke		Equipment Sr. No: GAMMATEC SN00810				
Cal. Validity: Prior to Job						
Type of Current: N/A		Lifting Power of Yoke: 18.1 KG				
Sensitivity: ☒ Burnish Strip ☐ Pie Gauge III Lines Visible						
Source of Light: Day light		Light Intensity: ≥ 1000 lux min				
Consumables: MAKE: MAGNAFLUX						
Cleaner: MAGNAFLUX SKC-S		White contrast: MAGNAFLUX WCP-2				
Batch No: 240706 BBE		Batch No: 240702 BBE				
Validity: JULY-2027		Validity: JULY-2027				
Magnetic Ink: MAGNAFLUX 7 HF		Batch No: 240705 BBE				
Validity: JULY-2027						
Item Description/Line No./ Drawing No.	Weld No	Welder No	Size	Sch. / WT	Observation (Map or Record of Indication)	Result (Acc. /Rej.)
REGISTRATION NO & OWNER ID NO: - 6395 LD / TER 1537 (FORKLIFT-MAKE: HANGCHA, 2020)						
FORK BLADE ID NO: 20610 (QTY-01 PAIR)	N/A	N/A	N/A	N/A	NO RELEVANT INDICATION OBSERVED	ACCEPTABLE

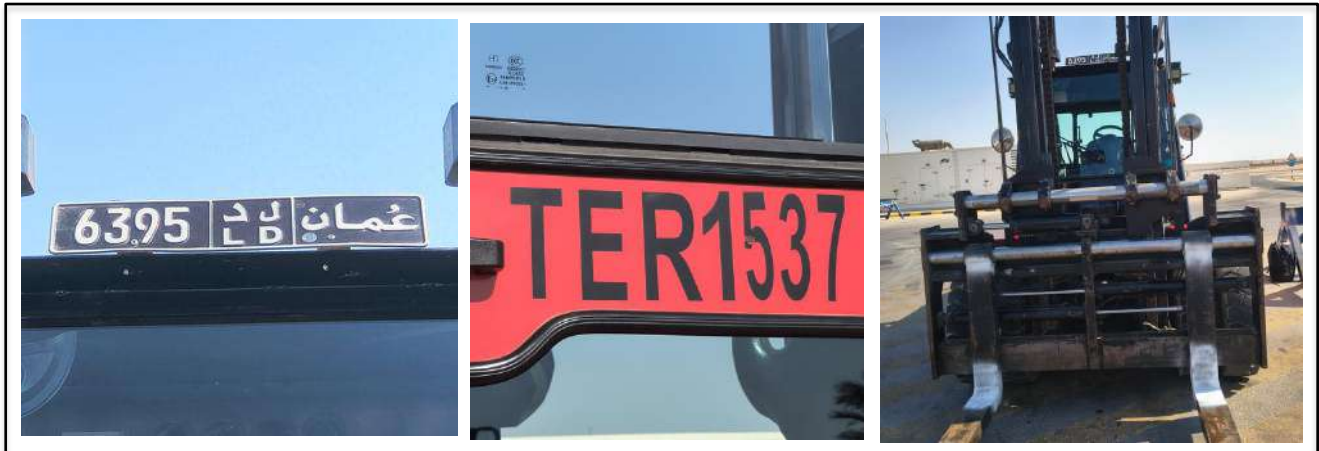

"MPI TEST CARRIED OUT SATISFACTORILY, FOUND NO RELEVANT INDICATIONS AT THE TIME OF INSPECTION"

LATEST DATE BY WHICH NEXT MPI MUST BE CARRIED OUT:		29/12/2026
Hi-Tech Inspection Services LLC	Contractor	Client/ TPI /AI
Signature:	Signature:	Signature:
 		
Name: HRISHIKESH MOHANAN	Name:	Name:
Qualification: MPT Level II		
Date: 30/12/2025	Date:	Date
